

Work Order ID 163532

Tuesday, June 27, 2017 1:31:35 PM

163532

Page 1

Item ID: D3594-044 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Floor Doubler Assembly, RH
Start Date: 6/27/2017 Start Qty: 4.00 ***4*** Cust Item ID:
Required Date: 7/4/2017 Req'd Qty: 4.00 ***4*** Customer:
Reference:

Approvals: Process Plan: DAS 21 9-89 Date: JUN 28 2017 Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D3594	D								
100	FLOW WATER JET	0.01							
100									
Waterjet	Memo	0.19							
FLOW CNC Waterjet	1-Cut as per Dwg D3594								
	Dwg Rev: <u>B</u>								
	Prog Rev: <u>B</u>								
	2-Deburr if necessary								
110	QC2- Inspect parts off machine FAI/FAIB	0.00							
110									
QC	Memo	0.04							
Quality Control									
120	QC8- Inspect parts - second check	0.00							
120									
QC	Memo	0.08							
Quality Control									

④

SC 17/07/04
DAS
45
9-89

④

SC 17/07/04
DAS
45
9-89

4

DAS
38
9-89
JUL 04 2017

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐								
Misidentified ☐	Past Due ☐								
OTHER : _____									

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
OTHER : ☐									

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
OTHER : ☐									

Work Order ID 163532

Tuesday, June 27, 2017 1:31:35 PM

163532

Page 4

Item ID: D3594-044 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Floor Doubler Assembly, RH
Start Date: 6/27/2017 Start Qty: 4.00 ***4*** Cust Item ID:
Required Date: 7/4/2017 Req'd Qty: 4.00 ***4*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
190	Identify as per dwg & Stock Location: <i>SKSCH</i>	0.00				<i>4</i>		<i>DAS 6 9-88</i>	<i>JUL 19 2017</i>
190									
Packaging	Memo	0.04							
Packaging									
200	QC21 - Final Inspection - Work Order Release	0.00							
200									
QC	Memo	0.40							<i>17/7/20</i>
Quality Control									

*DAS
21
9-88**JUL 19 2017*

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																																																										
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Tuesday, June 27, 2017 1:31:38 PM

Page 1

Work Order ID: 163532

163532

Parent Item: D3594-044

D3594-044

Parent Item Name: Floor Doubler Assembly, RH

Start Date: 6/27/2017

Required Date: 7/4/2017

Start Qty: 4.00

Required Qty: 4.00

Comments: IPP Rev :A New Issue 07-01-22 EC
16.07.28 NEW ISSUE DD VERF:JLM
AS PER DWG REV.D DD VERF:JFS

IPP REV:B
IPP REV:C 17.04.27

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M6061T6S.080		Purchased	No			100	sf	83.2500	0.51	2.147368			
M6061T6S 080										**		5c 17/07/04	
6061-T6 .080 Sheet												DAS	
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				MAT020				83.25					45
				m136342				42.75					9-89
				m136632				0.3					
				m137263				12.1		2.2			
				m137513				28.1					
MS20426AD4-4		Purchased	No			170	Each	2,520.000	2	8			
MS20426AD4-4										**		17/07/13	DAS
Rivet													36
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			9-89
				GA				1041					
				125445				1041		8			
				ST312				1479					
				m132536				1479					
MS21069-5		Purchased	No			170	Each	11.0000	1	4			
MS21069-5										**		17/07/13	DAS
Anchor nuts													36
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			9-89
				ST299				11					
				m137587				11		4			

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE




QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval				
Description Work Order Deviation				Disposition				Completed By			
								Lead hand / Supervisor Approval Verification			
								QC / QA Coordinator Approval			
Root Cause		FAULT CATEGORY									
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐						
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐						
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐						
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐						
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐						
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐						
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐						
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐						
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐						
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐						
Past Expiry Date ☐	Manufacturing Process ☐										
Misidentified ☐	Past Due ☐	OTHER :									

ITEM	QTY -041	P/N	DESCRIPTION
	X	D3594-041	DOUBLER ASSEMBLY
1	1	D3594-1	DOUBLER
2	1	MS21089-5	NUT PLATE, SELF-LOCKING
3	2	MS20426AD4-4	RIVET, SOLID, CSK

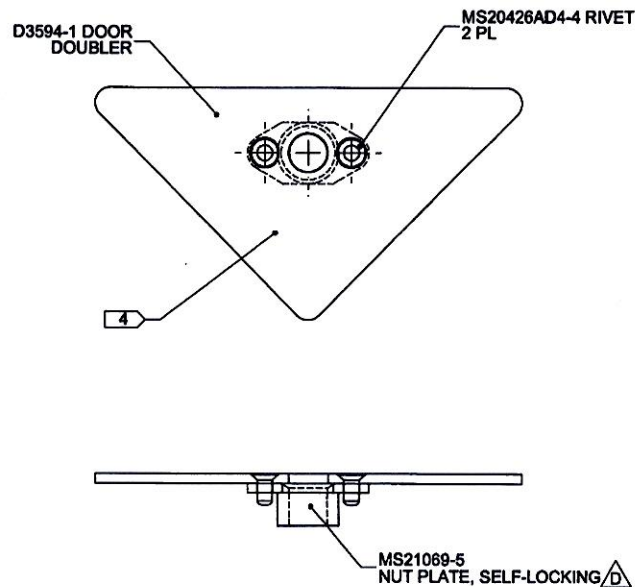

D3594-041 DOOR DOUBLER ASSEMBLY


NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044
- 7) WEIGHT: 0.04 lbs

RELEASED


2017 APR 27 *qf*
ECN 16-673

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 163532 MJS
1706-28




D	MS20189-5 WAS MS21068L3 (ZN D6-1, B3-1, D6-3, D3-3, C5-3, C4-3). REF PAR16-557	VS	17.04.07
C	REFORMAT TO CURRENT STANDARDS. ADD 0.5" OF MATERIAL TO -3 & -4 REASON PAR16-501.	AJS	16.05.25
B	REFORMAT TO B SIZE DRAWING. SHEET 2 ADD -5.	AJS	08.05.14
A	NEW ISSUE	MB	07.04.13
REV.	DESCRIPTION	BY	DATE
DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	VS		
CHECKED	HS	DRAWING NO.	REV. D
MFG. APPR.	DD	D3594	SHEET 1 OF 4
APPROVED	DSW	TITLE	SCALE
DE APPR.	N/A <i>WJ</i>	DOUBLER	NTS
DATE	17.04.07	COPYRIGHT © 2007 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	


APPROVED

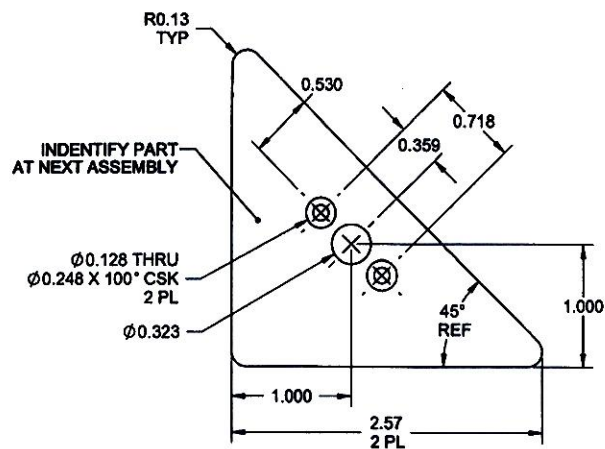

D3594-1 DOOR DOUBLER

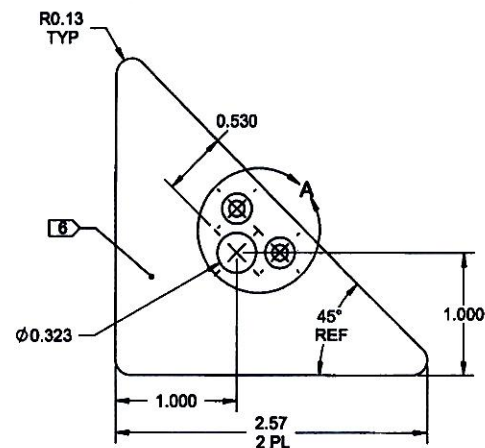

D3594-5 DOOR DOUBLER

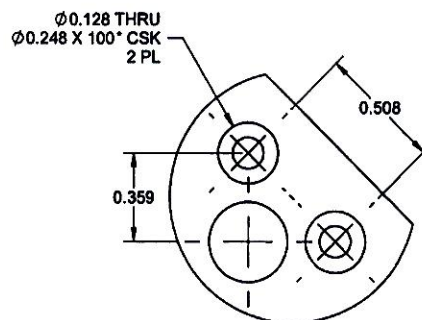

DETAIL A
SCALE 2X

NOTES:

- 1) MATERIAL: 6061-T6 (OR 6061-T62) ALUMINUM SHEET, 0.080 THICK, PER AMS-QQ-A-250/11 OR AMS 4025 OR AMS 4027 REF. DART SPEC. M6061T6S.080
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION -5 ONLY: IDENTIFY PER DART QSI 044
- 7) WEIGHT -1/-5: 0.03 lbs

RELEASED


2017 APR 27

APPROVED


DESIGN	MB	DART AEROSPACE LTD	
DRAWN	VS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	HS	DRAWING NO.	REV. D
MFG. APPR.	DD	D3594	SHEET 2 OF 4
APPROVED	DSW	TITLE	SCALE
DE APPR.	N/A <i>92</i>	DOUBLER	NTS
DATE	17.04.07	COPYRIGHT © 2007 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

ITEM	QTY -043	P/N	DESCRIPTION
	X	D3594-043	FLOOR DOUBLER ASSEMBLY
1	1	D3594-3	DOOR DOUBLER ASSEMBLY
2	2	MS20426AD4-4	RIVET, SOLID, CSK
3	1	MS21069-5	NUT PLATE, SELF-LOCKING

ITEM	QTY -044	P/N	DESCRIPTION
	X	D3594-044	FLOOR DOUBLER ASSEMBLY
1	1	D3594-4	DOOR DOUBLER ASSEMBLY
2	2	MS20426AD4-4	RIVET, SOLID, CSK
3	1	MS21069-5	NUT PLATE, SELF-LOCKING

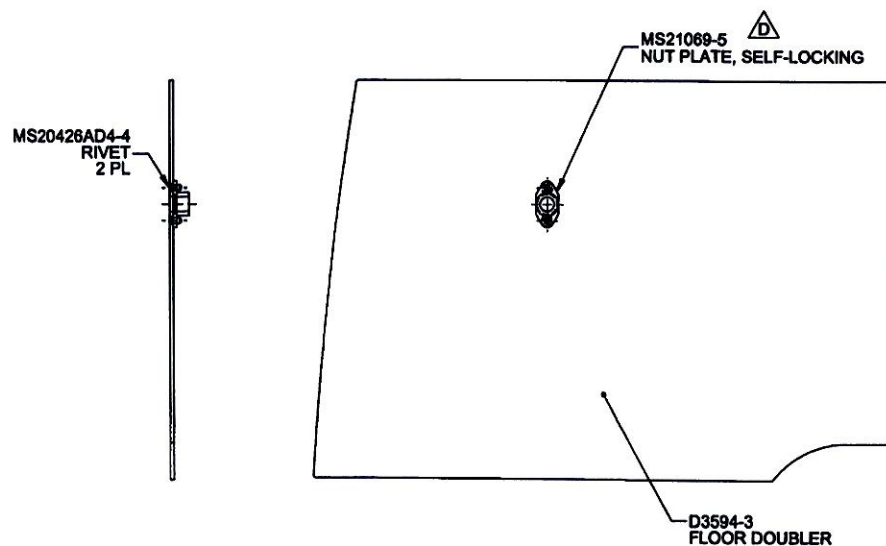

D3594-043 FLOOR DOUBLER ASSEMBLY

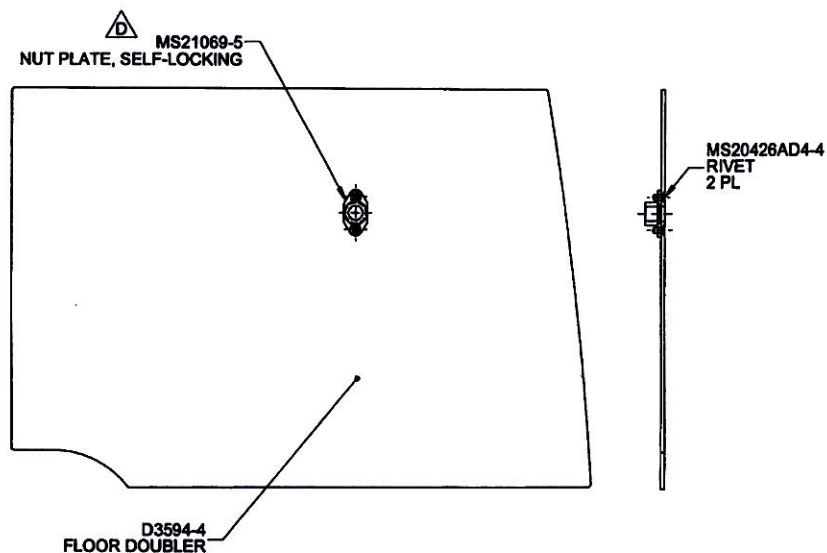


D3594-044 FLOOR DOUBLER ASSEMBLY

NOTES:
 1) MATERIAL: NONE
 2) FINISH: N/A
 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 5) BREAK SHARP EDGES: N/A
 6) IDENTIFICATION: IDENTIFY PER DART QSI 044
 7) WEIGHT: 0.82 lbs

RELEASED
 2017 APR 27

APPROVED

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	VS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	HS	DRAWING NO.	REV. D
MFG. APPR.	DD	D3594	SHEET 3 OF 4
APPROVED	DSW	TITLE	SCALE
DE APPR.	N/A	DOUBLER	NTS
DATE	17.04.07	COPYRIGHT © 2007 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR DISSEMINATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

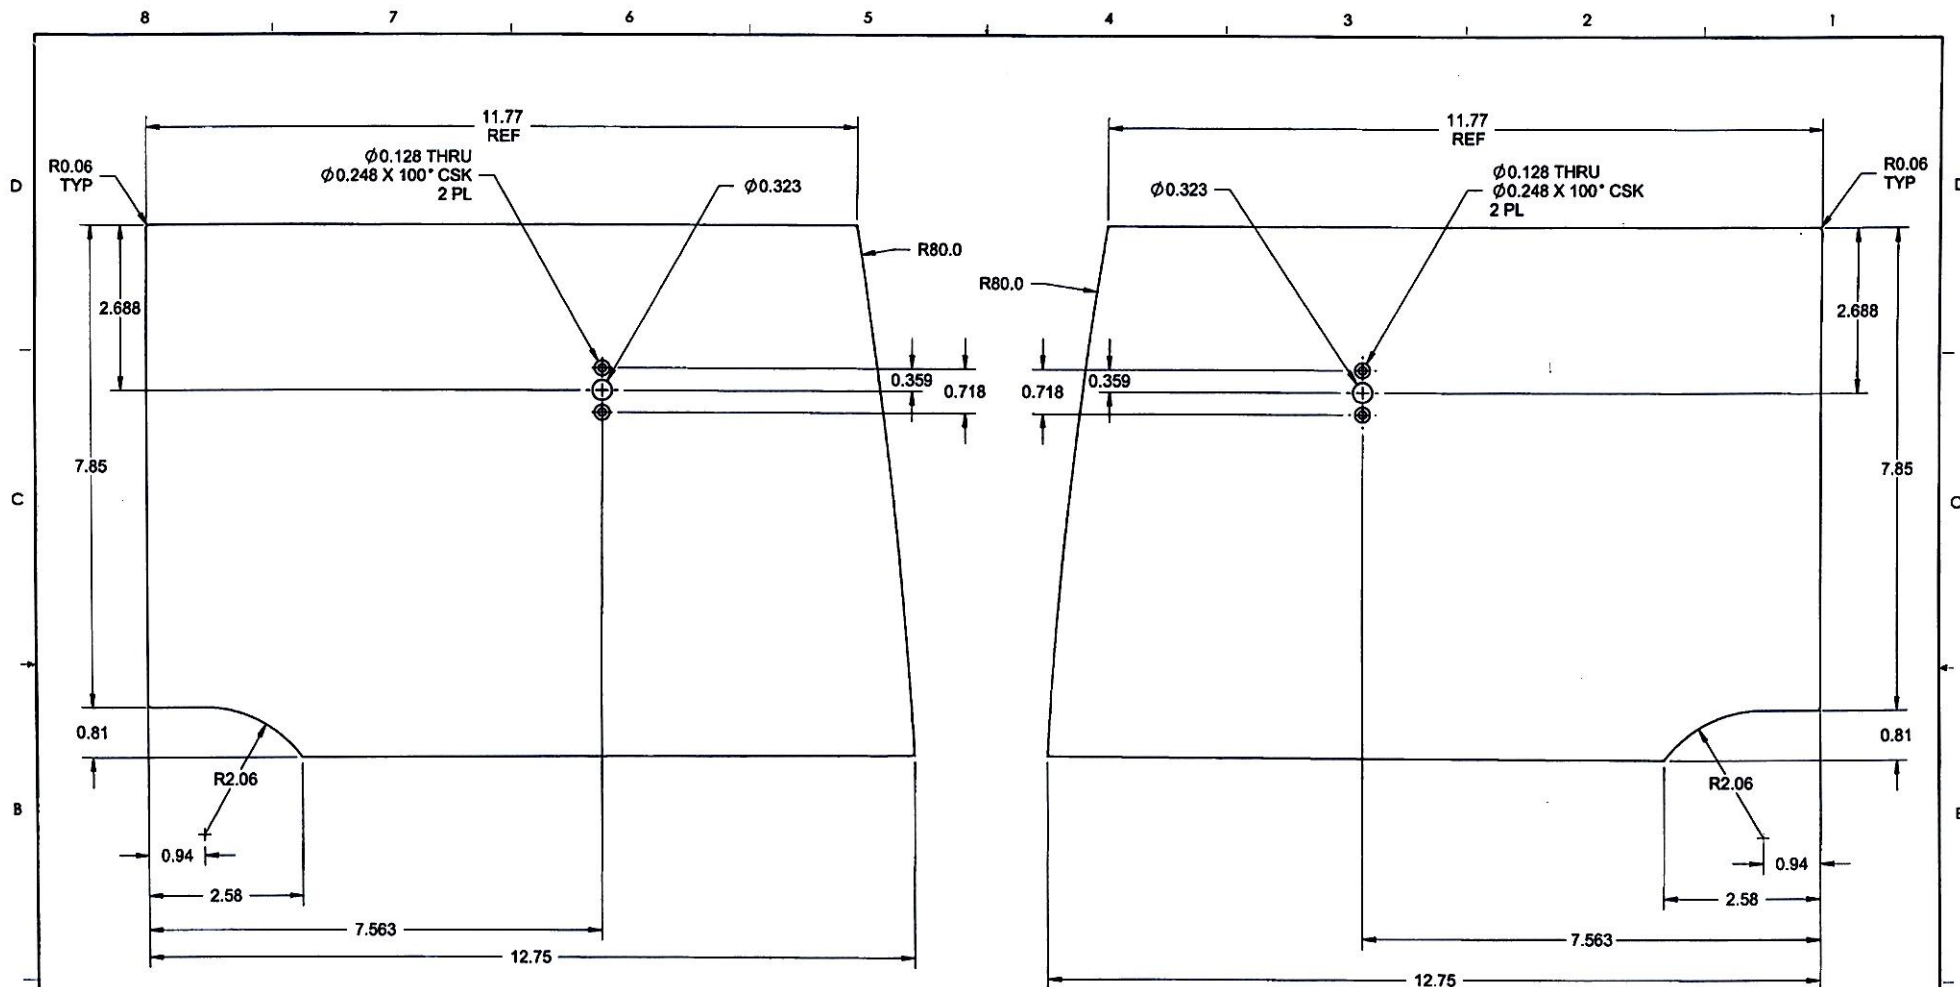

D3594-3 FLOOR DOUBLER

D3594-4 FLOOR DOUBLER

NOTES:

- 1) MATERIAL: 6061-T6 (OR 6061-T62) ALUMINUM SHEET, 0.080 THICK, PER AMS-QQ-A-250/11 OR AMS 4025 OR AMS 4027 REF. DART SPEC. M6061T6S.080
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY AT NEXT ASSEMBLY
- 7) WEIGHT: 0.82 lbs

RELEASED

2017 APR 27

APPROVED

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	VS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	HS	DRAWING NO.	REV. D
MFG. APPR.	DD	D3594	SHEET 4 OF 4
APPROVED	DSW	TITLE	SCALE
DE APPR.	N/A PLD	DOUBLER	NTS
DATE	17.04.07	COPYRIGHT © 2007 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			
